STEERING COMMITTEE CORE BELIEFS

- 1. The plan must address the critical infrastructure systems within the buildings (warm, safe, dry) as a first priority.
- 2. This facilities plan requires action and cannot be deferred.
- 3. The facilities plan must address the curb appeal and aesthetics of the buildings in order to compete with charter schools.
- 4. The plan must geographically defend against charter school's locations.
- 5. The plan must reconfigure the grade structure to better meet educational needs.
- 6. The investment in facilities must not reduce investment in the other 3 pillars of district strategy (Achievement, Finance, Climate).
- 7. The plan must fit the School Board's ability to fund the plan within its current Act 1 taxing authority (not a referendum).
- 8. The plan must be focused on helping the district save money on operating costs.

ICS with SCHRADERGROUP

JANUARY 2023 MFP SESSION RANKING OF CRITICAL ELEMENTS

- 1. The facilities plan should be tilted towards new construction versus renovation/addition.
- 2. The correct configuration of the CAIHS and CASH Campus is 9-10 & 11-12.
- 3. Scott cannot be used as an Elementary School.
- 4. Classroom trailers should be removed / replaced with a permanent solution.
- 5. The facilities solutions must contain two separate middle schools.
- 6. Caln is beyond repair and should be closed.
- 7. East Fallowfield is beyond repair and should be closed.

King's Highway Elementary School

Rainbow Elementary School

Coatesville Area Senior High School 9-10 Center Friendship Elementary School

North Brandywine Middle School Reeceville Elementary School

Gordon Education Center Scott Middle School

Caln Elementary School

Coatesville Area Senior HighSchool 11-12 Center

South Brandywine Middle School

East Fallowfield Elementary School



King's Highway addition and renovations Elementary School ES

Steering Committee Final Building Option

Rainbow Elementary School

Coatesville Area Senior High School 9-10 Center

MS

Gordon Education Center Scott Middle School

MS North Brandywine Middle School demo existing North Brandywine Middle School FS **Reeceville Elementary School** middle school addition

new middle school

Coatesville Area Senior HighSchool 11-12 Center

JOUTH DI MINU WING MIMMIC SCHOOL

new elementary school demo existing middle schol

allowfield Elementary School



ES

FEBRUARY 2023 MFP TAKE AWAYS

Phase 1 - New Elementary School south of Rt. 30

- Attractive to families for students starting in Kindergarten in lieu of Charter
- If East Fallowfield closes, a new school will keep those families in the district
- District-owned land available at South Brandywine site
- Cannot take Scott off-line asset too costly to replace; renovations required
 - Use both Scott and N. Brandywine for 6-8 Middle Schools
- Immediate solution has to have some commitment to Middle School (not just ES)
 - Add new classroom wing onto to N. Brandywine MS for future new school
 - Pull 8th grade off campus ASAP

GRADE ALIGNMENT / BUILDING INVENTORY (AT CONCLUSION OF PLAN)

• (4) K-5 ELEMENTARY SCHOOLS

- Kings Highway ES Full renovations (warm/safe/dry); remove modulars
- Reeceville ES Add 8 classrooms
- Rainbow ES No work proposed
- S. Brandywine ES New construction
- Close Caln and East Fallowfield Elementary Schools

• (2) 6-8 MIDDLE SCHOOLS

- Scott MS Renovations (warm/safe/dry)
- N. Brandywine MS New construction
- Return Campus to 9-10 CAISH and 11-12 CASH

OPTION 1: PHASE 1 – ESs; 6-8 PHASE 2 – NEW MS

PHASE 1

- Split 6-8 population to Scott and NBMS
- Kings Highway ES renovations
- Reeceville Elementary School additions
- New N. Brandywine classroom wing
- Scott renovation
- New Elementary School
- Close Caln and East Fallowfield ES

PHASE 2

Remaining NBMS new construction
Jan 2029

<u>Complete</u> Fall 2024 Fall 2025 Fall 2025 Fall 2025 Fall 2026

- Dec 2026
- Dec 2026

OPTION 1: PHASE 1 – ESs; 6-8 PHASE 2 – NEW MS

PROS

8th Grade moves off-campus as soon as possible

CHALLENGES

- Scott and N. Brandywine at full capacity
 - Proposed classroom wing addition not complete
 - No room internal to Scott to move students around to renovate; where to locate temporary classrooms during construction? Added costs for modulars.

OPTION 2: PHASE 1 – ESs; 6-7 PHASE 2 – NEW MS

PHASE 1

- Split 6-7 population to Scott and NBMS
- Kings Highway ES renovations
- Reeceville Elementary School additions
- New N. Brandywine classroom wing
- Scott renovation
- New Elementary School
- Close Caln and East Fallowfield ES

PHASE 2

Remaining NBMS new construction
Jan 2029

<u>Complete</u> Fall 2024 Fall 2025 Fall 2025 Fall 2025 Fall 2026

- Dec 2026
- Dec 2026

OPTION 2: PHASE 1 – ESs; 6-7 PHASE 2 – NEW MS


PROS

- Less transitions two grades at Scott and N. Brandywine Middle Schools (6-7)
- Combining grades 6-7 offers students mentorship
- Scott and N. Brandywine not at full capacity with two grade levels
 - Schedule allows large part of Scott to be renovated before 8th grade is added
 - Swing space at Scott available to move students around to renovate

CHALLENGES

8th Grade moves off-campus in Fall 2025

Construction Plan Phase 1 – Move to 6/7 ASAP

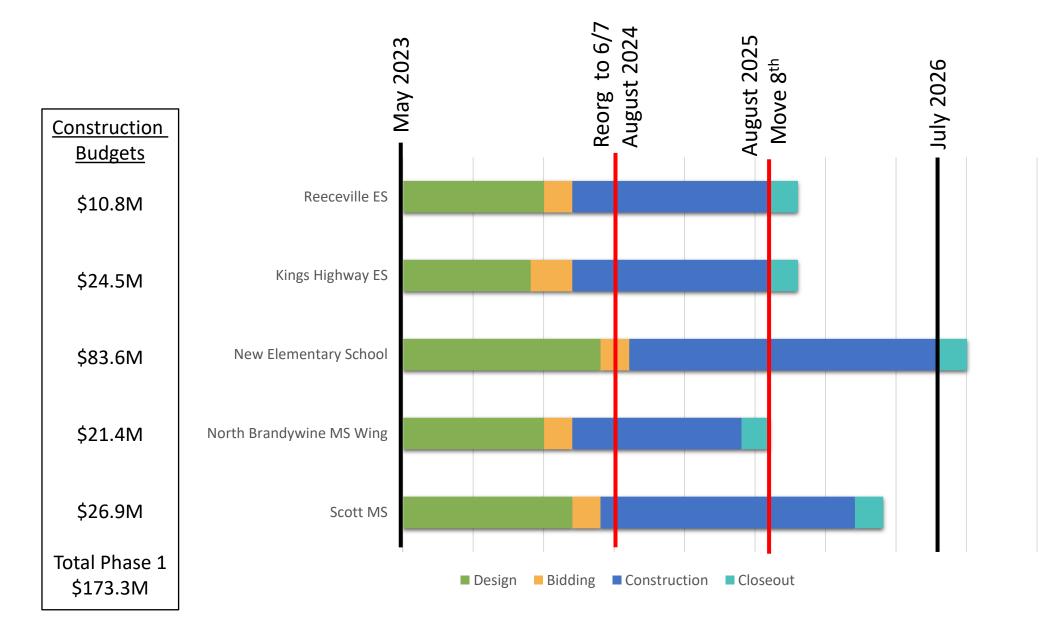

Construction Plan Phase 1& 2

